




Cree Trappers' Association
47th Annual General Assembly Wemindji
August 20, 2025

CABIN REBUILD PROJECT 2024- 2026

- They are total of 311 traplines, 183 traplines were affected by 2023 forest fires, and a total of 142 cabins were reported as impacted.

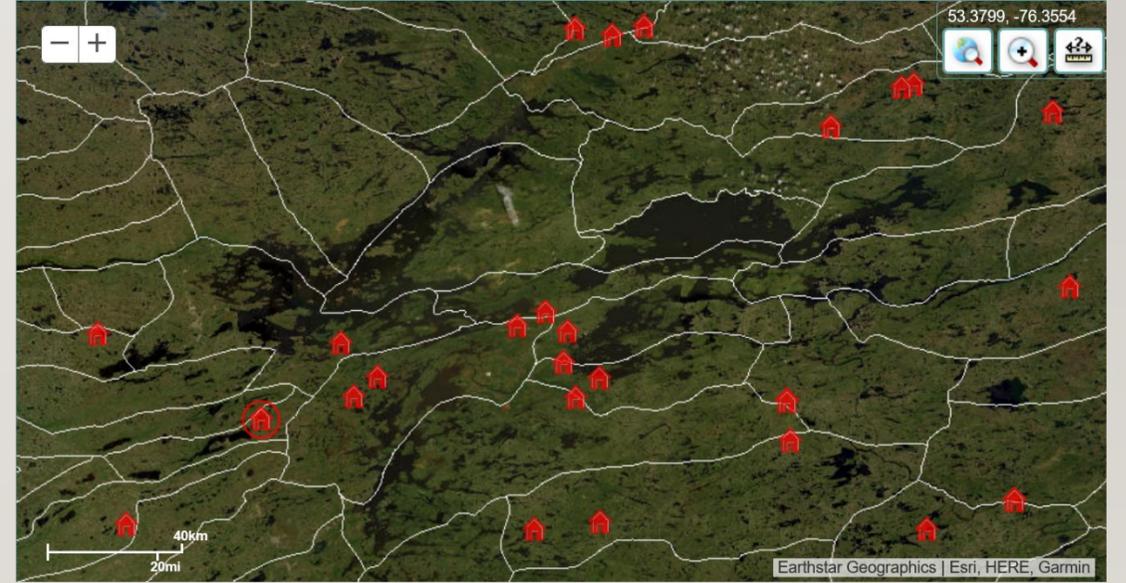

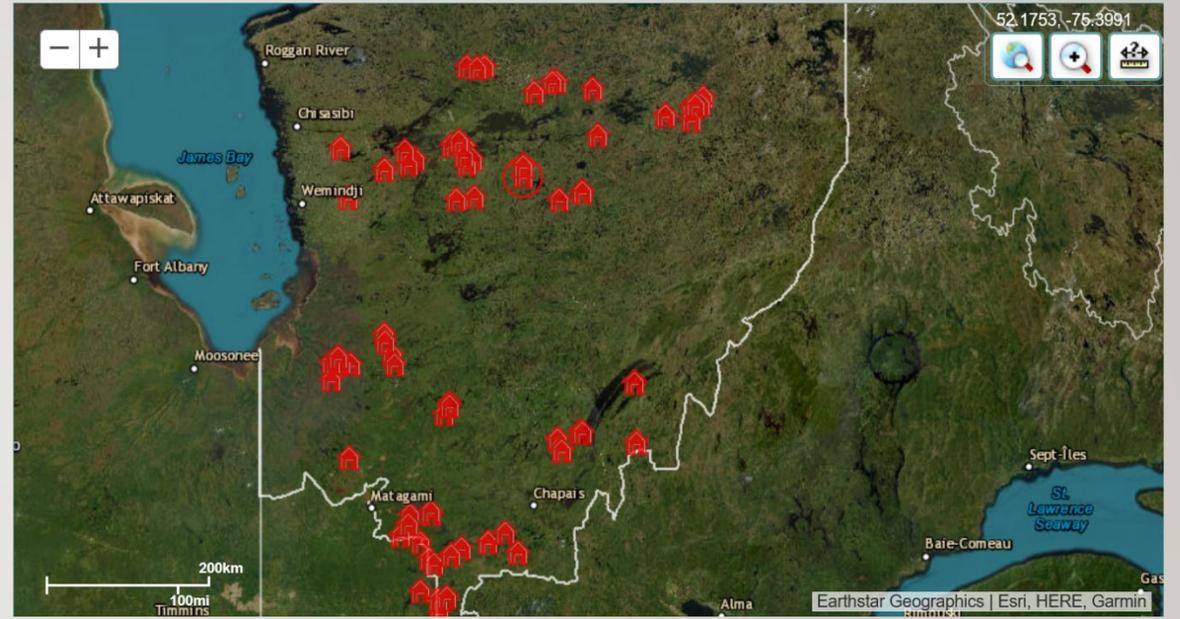

CREE TRAPPERS ASSOCIATION
REBUILD CABIN PROJECT 2024-2025
SUMMARY REPORT



	# Cabins	# of Cabins finished	Budget	Actual Cost	Balance
Chisasibi	10	10	\$ 409,046.00	\$ 363,836.38	\$ 45,209.62
Mistissini	16	16	\$ 853,139.00	\$ 764,108.09	\$ 89,030.91
Nemaska	3	3	\$ 112,310.00	\$ 119,944.89	\$ (7,634.89)
Waskaganish	8	8	\$ 246,216.00	\$ 250,788.20	\$ (4,572.20)
Waswanipi	7	7	\$ 218,013.00	\$ 206,201.48	\$ 11,811.52
Wemindji	6	6	\$ 192,642.00	\$ 196,706.57	\$ (4,064.57)
Sub-Total	50	50	\$ 2,031,366.00	\$ 1,901,585.61	\$ 129,780.39
Other Expenses			\$ -	\$ 63,916.44	\$ (63,916.44)
Administration Fees			\$ -	\$ 40,000.00	\$ (40,000.00)
TOTAL			\$ 2,031,366.00	\$ 2,005,502.05	\$ 25,863.95

FUNDING

CNG	\$ 400,000.00
Niskamoon Corporation	\$ 712,634.58
Eenou-Eeyou Community Foundation	\$ 42,867.47
Cree Hunters Economic Security Board	\$ 400,000.00
RIFF - Mining Companies	\$ 200,000.00
CTA	\$ 250,000.00
TOTAL	\$ 2,005,502.05

CREE TRAPPERS ASSOCIATION

REBUILD CABIN PROJECT BUDGET 2025-2026



	# Cabins	# Cabins Shipped	# of Cabins finished	Budget
Chisasibi	10	7	1	\$ 619,038.70
Eastmain				\$ -
Mistissini	20	10	8	\$ 838,077.40
Nemaska	3	1		\$ 184,115.48
Ouje-Bougoumou	2	1		\$ 69,807.74
Waskaganish	5	3	3	\$ 174,519.35
Waswanipi	5	3	2	\$ 174,519.35
Wemindji	5	3		\$ 174,519.35
Whapmagoostui				\$ -
Sub-Total	50	28	14	\$ 2,234,597.37
Other Expenses				\$ -
Administration Fees				\$ -
TOTAL				\$ 2,234,597.37

FUNDING

CNG				\$ -
Niskamoon Corporation				\$ 787,365.00
CTA				\$ 250,000.00
TOTAL				\$ 1,037,365.00



Rebuild Cabin Project 2025–2026.

- **Planned cabins: 50**
 - **Cabins shipped so far: 28**
 - **Cabins finished: 14**
 - **Total budget required: \$2,234,597.37**
 - **Funding secured so far:**
 - Niskamoon Corporation: **\$787,365.00**
 - CTA: **\$250,000.00**
 - CNG: **(not yet confirmed or contributed)**
 - **Total confirmed funding: \$1,037,365.00**
- ➔ This leaves a **shortfall of \$1,206,232.37** to fully fund the project.

At this time, we have suspended the Cabin Rebuild Project until we can get funding from the Cree Nation Government.

CABIN INSURANCE 2025-2026



The regional CTA are working with BOC for the new Insurance for our Hunters and Trappers for this year's coverage



CTA will likely subsidized 50% on the cabin insurance program.



Contact Local CTA Administrator if your looking to get insurance for your cabin.



